Existing Sakura: the space behind the problem

Source a0fb347. Room/fixture envelopes, not construction walls. Metres; scale 1:100 at A3 / 100%.

01 / GROUND FLOOR

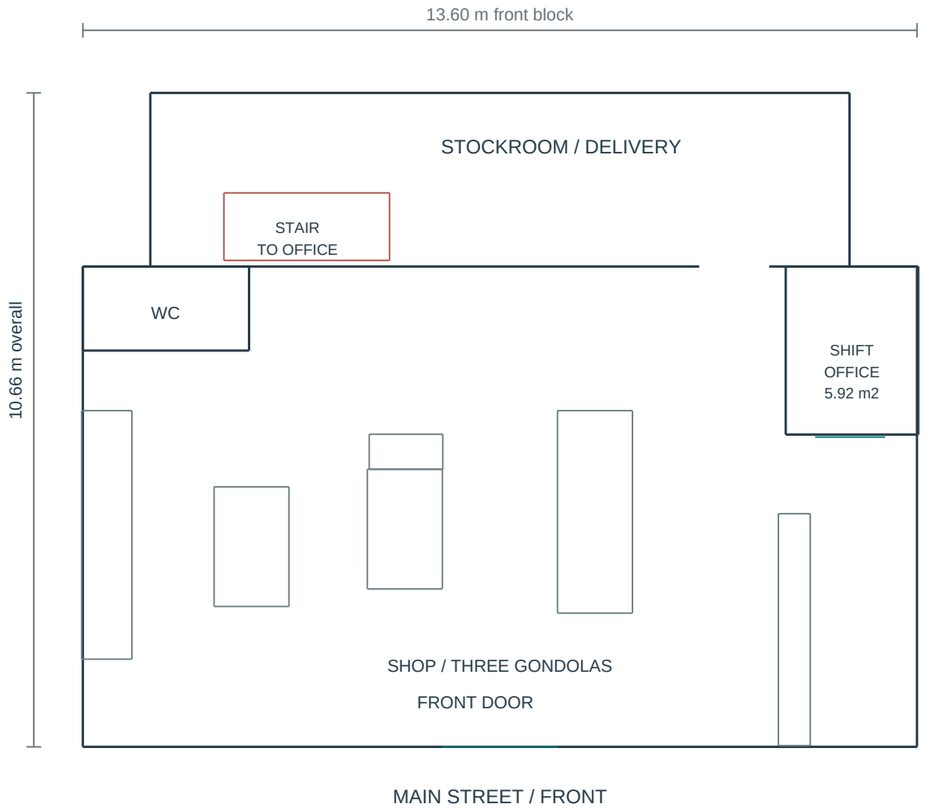

02 / UPPER FLOOR

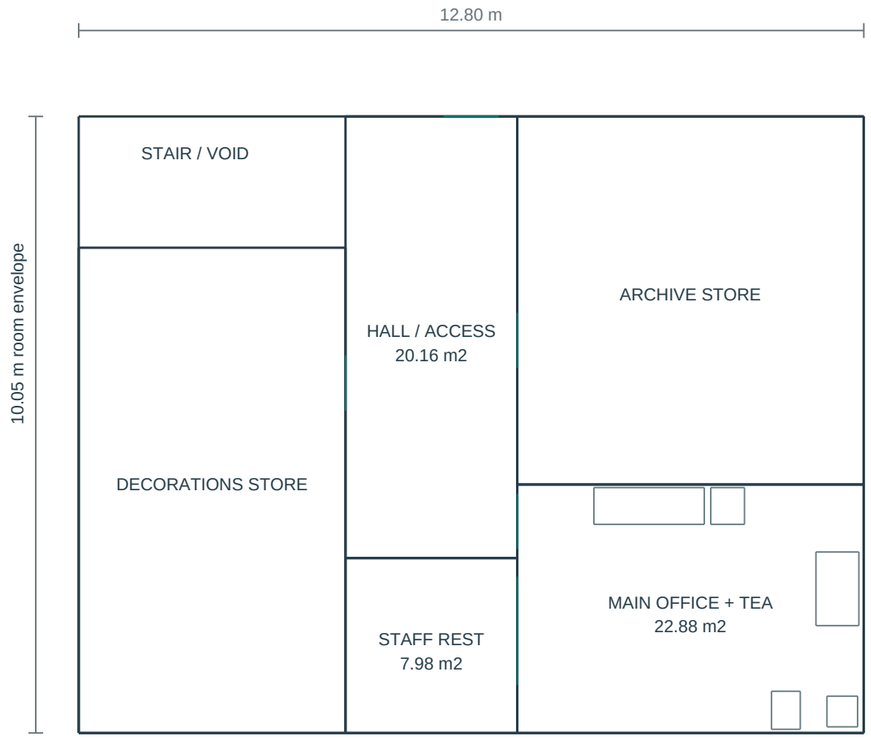

Teal markers: existing openings. Room envelopes shown; door swings and wall build-ups omitted.

Audit findings

Ground polygon: 138.75 m2. Front block: 106.49 m2, including the small office and WC; not net retail area.

Upper room envelope: 128.64 m2. External upper-shell nominal depth is 11 m; the office room itself is 10.05 m deep.

Both offices together: 28.80 m2. The upstairs also owns archive, decorations, tea facilities and staff rest functions.

The stair defect is only one symptom: the building programme is much larger than the compact reference shop.

A compact single-storey Sakura: discussion option

UNAPPROVED ZONING CONCEPT. New dimensions and fixture positions are proposals; access unvalidated. Scale 1:100.

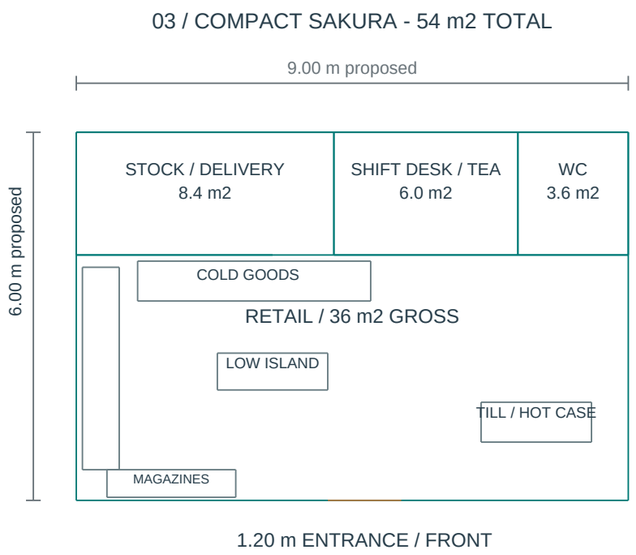

Why this is closer to Tomato

Reference study: Tomato / DCBN shell 8.03 x 4.23 m, about 34 m2, ceiling 2.41 m. These are prior recorded model measurements, not newly surveyed here.

The proposed retail block is 36 m2 gross with one low central island, readable perimeter goods and a till by the entrance. The full 54 m2 proposal includes 18 m2 of support rooms; it is not a direct copy of the 34 m2 shell.

Keep Sakura original: Thuan, the shop identity, door chime, stock families, local signage, hot food, magazines and small personal details. Take spatial economy and atmosphere from Tomato.

Keep shift administration beside the till. Move monthly accounts and archives only if a separate terminal suite is approved. Do not make Thuan leave customers to process a sale.

Target clear primary circulation around 1.2 m; validate shelf access, queue, delivery trolley, avatar bodies and camera boom in a mock-up before committing to these fixture positions.

Lower-risk alternative

First remove or repurpose the upper storey while keeping the current street footprint, front door and shop anchors. This reduces migration risk, but does not by itself deliver Tomato-like scale. A later frontage/room shrink needs a deliberate ground-plan and neighbour-spacing revision.

Decision still required: retain today's footprint, or commit to a compact shop? The drawing is a discussion layout, not a collision-tested implementation.

Ferry terminal: possible destination, not vacant space

Existing exterior footprint at 1:100; room schematics are separate coordinate frames. Preserve harbour operations.

Confirmed mismatch

Exterior waiting hall: 4.1 x 7.3 m = 29.93 m2. Interior builder: 9 x 7 m = 63 m2 before bounds insets. The interior therefore has about 2.1 times the exterior hall area. Rotation alone cannot resolve that.

Existing Harbour Office is a separate 6.74 x 6.74 m interior reached by the hall's office interaction. The exterior upper shell is 6.7 x 6.9 m, labelled as records space; no corresponding enterable upper-room layout was found in the inspected builders.

Do not move Sakura into the passenger waiting area or replace the Harbour Office. Ticketing, post/parcels, Ganaha's counter, benches, departures and crew routines must remain usable.

Preferred relocation concept

04 / CURRENT EXTERIOR - WORLD FOOTPRINT

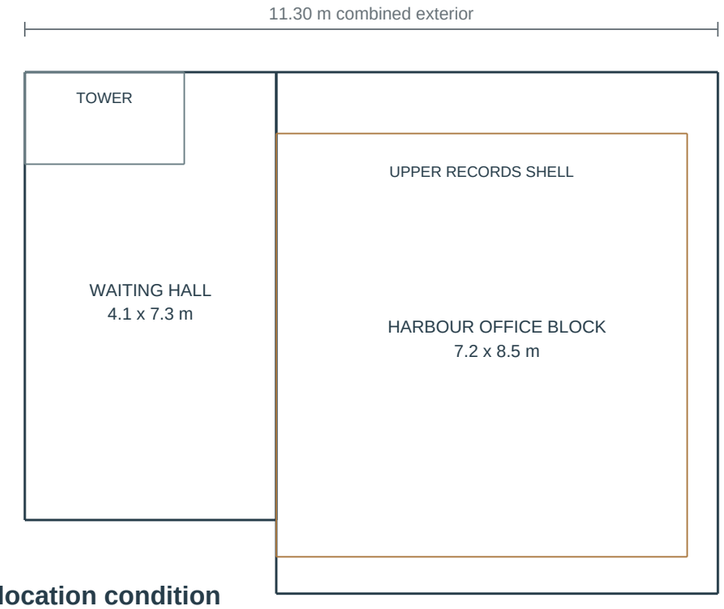

05 / POSSIBLE UPPER SUITE

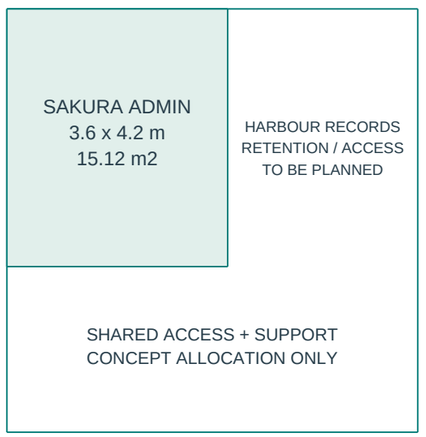

Relocation condition

Reconcile exterior, interiors and actual access first. Then allocate a separate Sakura Trading office, retaining harbour records. Terminal rest/tea facilities are optional and require a decision. No displacement or vacant-space assumption is authorised.

Audit recommendation and change protections

Source-based design review. No game code, room geometry, schedules or saves were changed in this audit.

Recommendation

Treat Sakura as a compact shop, not a combined shop, head office, warehouse and staff accommodation. Keep a useful shift office beside Thuan's till. A single storey is a credible direction, subject to your decision.

Move business administration to a separately identified Sakura Trading suite at the Port Building only after its mismatched room/exterior plans and records-space ownership are resolved. The ground-floor Harbour Office remains a working harbour office.

Give removed upstairs functions explicit destinations: till cash/security stays near the shop; current account books remain at the shift desk; monthly books can go to the terminal; decorations and bulk supplies are candidates for the existing Sakura Trading depot. Verify depot capacity before assigning them.

Do not silently remove the rest-room feature: decide whether it is retained at Sakura, shared at the terminal, or retired. It is staff rest space, not Thuan's home; her home remains on Kitano-jima.

Implementation sequence after decisions

1. Freeze the intended size and room functions. Keep PR #364 (stair repair) separate; decide whether it remains an interim repair or is superseded by the approved single-storey redesign.

2. Draw one coherent exterior/interior/access plan for both sites. Mock up room sizes with actual avatars, stocked fixtures, a queue and the third-person camera. Do not scale props or avatars to force a fit.

3. Preserve stable site/product identities and transactions. Migrate saves in sakura-office to a safe retained room; map old office destinations explicitly. Keep purchases, unpaid basket contents, money, relationships and day progression.

4. Update the whole ownership chain together: upper facade, roof, fire escape, stair opening, prompts, portals, signage, comic places, shop routines, paperwork and tests. An empty upper shell or an orphaned door is not a completed removal.

5. Revalidate enter/exit, camera, shelves, deliveries, NPC routes, quiet HUD, shop hours, ferry/terminal services, saves, ground audit and z-fighting. Capture actual game before/after at 390 x 844 and desktop before owner review.

Evidence / limits

Measured digital plans: sakura-layout.js, sakura-shell.js, sakura-small-office.js, sakura-office-room.js, port-building.js, port-hall.js and supplied-rooms.js at main a0fb347. Existing fixtures are selected plan footprints, not a complete inventory. Reference: docs/research/new-yokosuka-lessons.md (19 October) and current brynnb/new-yokosuka DCBN collision metadata. No source assets were copied.

Concurrent work: PR #362 changes Sakura staffing/trade and proposed hours. PR #364 repairs the stair but is still unmerged. Coordinate these before implementation. No new physical-device walkthrough or proposed-layout collision acceptance is claimed.
